


Revitalization of the Lincoln School
 Preliminary Project Schedule
 Design Development to Construction Phase

ID	Task Name	Duration	Start	Finish	2019	2020	2021	2022	2023
1	DESIGN DEVELOPMENT	113 days	12/4/2018	5/13/2019					
2	Schematic Design Confirming Estimate by CM	11 days	12/4/2018	12/18/2018					
3	Develop Design Development Documents to Estimator	73 days	12/4/2018	3/18/2019					
4	Design Development Cost Estimate	11 days	3/18/2019	4/1/2019					
5	Reconciliation and Value Engineering	8 days	4/1/2019	4/10/2019					
6	Submit Design Development Documents to OPM, CM and Cx for Review	0 days	3/18/2019	3/18/2019	3/18/2019 ◆ Submit Design Development Documents to OPM, CM and Cx for Review				
7	OPM, CM and Cx Review	11 days	3/18/2019	4/1/2019					
8	Design Development Submission	0 days	4/29/2019	4/29/2019	4/29/2019 ◆ Design Development Submission				
9	Owner Review	12 days	4/26/2019	5/13/2019					
10	SITE PERMITTING	161 days	11/30/2018	7/17/2019					
11	Lincoln Conservation Commission - ANRAD	75 days	11/30/2018	3/18/2019					
12	Prepare Application Documents	4 days	11/30/2018	12/5/2018					
13	File Application	0 days	12/5/2018	12/5/2018	12/5/2018 ◆ File Application				
14	Hearings	19 days	12/19/2018	1/16/2019					
15	Conservation Commission Decision	26 days	1/16/2019	2/20/2019					
16	Appeal Period	10 days	2/20/2019	3/5/2019					
17	File at Registry	10 days	3/5/2019	3/18/2019					
18	Lincoln Conservation Commission - NOI	105 days	2/20/2019	7/17/2019					
19	Prepare Application Documents	31 days	2/20/2019	4/3/2019					
20	File Application	0 days	4/3/2019	4/3/2019	4/3/2019 ◆ File Application				
21	Hearings	21 days	4/17/2019	5/15/2019					
22	Conservation Commission Issue Order of Conditions	26 days	5/15/2019	6/19/2019					
23	Appeal Period	10 days	6/19/2019	7/2/2019					
24	File at Registry	10 days	7/3/2019	7/17/2019					
25	Lincoln Planning Board - Site Plan Approval, Scenic Roads Permit	111 days	1/23/2019	6/26/2019					
26	Prepare Application Documents	69 days	1/23/2019	4/29/2019					
27	File Application	0 days	4/29/2019	4/29/2019	4/29/2019 ◆ File Application				
28	Hearings	18 days	4/29/2019	5/22/2019					
29	Planning Board Issues Site Plan Approval and Permit	16 days	5/22/2019	6/12/2019					
30	Appeal Period	11 days	6/12/2019	6/26/2019					
31	File at Registry	11 days	6/12/2019	6/26/2019					
32	Lincoln Historical Commission - Demolition Delay Permit	84 days	12/4/2018	4/2/2019					
33	Prepare Application Documents	29 days	12/4/2018	1/15/2019					
34	File Application	0 days	1/15/2019	1/15/2019	1/15/2019 ◆ File Application				
35	Hearings	21 days	2/5/2019	3/5/2019					
36	Historical Commission Decision	21 days	3/5/2019	4/2/2019					
37	Massachusetts Historical Commission	64 days	12/4/2018	3/5/2019					
38	Prepare Project Notification Form	24 days	12/4/2018	1/8/2019					
39	File PNF	0 days	1/8/2019	1/8/2019	1/8/2019 ◆ File PNF				
40	MHC Review	21 days	1/8/2019	2/5/2019					
41	MHC Issues Decision	21 days	2/5/2019	3/5/2019					
42	BUILDING PERMITTING	99 days	8/30/2019	1/21/2020					
43	Modulars Permit	22 days	8/30/2019	10/1/2019					
44	Building Permit	23 days	12/18/2019	1/21/2020					

Revitalization of the Lincoln School
Preliminary Project Schedule
Design Development to Construction Phase




ID	Task Name	Duration	Start	Finish	2019	2020	2021	2022	2023
45	CONSTRUCTION DOCUMENTS	165 days	4/29/2019	12/18/2019					
46	Ceiling Removal and Abatement Package No. 1	0 days	4/29/2019	4/29/2019	4/29/2019				
47	Develop 60% Contract Documents to Estimator	65 days	4/29/2019	7/29/2019					
48	60% Contract Documents to OPM, CM and Cx for Review	0 days	7/29/2019	7/29/2019	7/29/2019				
49	OPM, CM and Cx Review	11 days	7/29/2019	8/12/2019					
50	60% Construction Documents Cost Estimate	11 days	7/29/2019	8/12/2019					
51	60% Construction Documents Submission	0 days	8/30/2019	8/30/2019	8/30/2019				
52	Owner Review	10 days	8/30/2019	9/13/2019					
53	Temporary Modulares Package No. 2	0 days	8/30/2019	8/30/2019	8/30/2019				
54	Develop 90% Contract Documents to Estimator	31 days	8/30/2019	10/14/2019					
55	90% Contract Documents to OPM, CM and Cx for Review	0 days	10/14/2019	10/14/2019	10/14/2019				
56	90% Construction Documents Cost Estimate	11 days	10/14/2019	10/28/2019					
57	OPM, CM and Cx Review	11 days	10/14/2019	10/28/2019					
58	90% Construction Documents Submission	0 days	11/15/2019	11/15/2019	11/15/2019				
59	Owner Review	8 days	11/15/2019	11/26/2019					
60	Construction Documents Complete Package No. 3	0 days	12/18/2019	12/18/2019	12/18/2019				
61	PROCUREMENT	252 days	3/4/2019	2/26/2020					
62	Prequalification - Package No. 2	74 days	3/4/2019	6/13/2019					
63	Develop Draft RFQs	22 days	3/4/2019	4/2/2019					
64	Submit Advertisement to Central Register and Local Newspaper	0 days	4/2/2019	4/2/2019	4/2/2019				
65	Notice in Central Register	0 days	4/10/2019	4/10/2019	4/10/2019				
66	Submit SOQs	0 days	5/9/2019	5/9/2019	5/9/2019				
67	Review SOQs	22 days	5/10/2019	6/10/2019					
68	Recommend Prequalified Subcontractors to SBC	0 days	6/12/2019	6/12/2019	6/12/2019				
69	Issue Notification Letters to Prequalified Subcontractors	0 days	6/13/2019	6/13/2019	6/13/2019				
70	Prequalification - Package No. 3	61 days	7/24/2019	10/17/2019					
71	Develop Draft RFQs (Subcontractors)	20 days	7/24/2019	8/20/2019					
72	Submit Advertisement to Central Register and Local Newspaper	0 days	8/20/2019	8/20/2019	8/20/2019				
73	Notice in Central Register	0 days	8/28/2019	8/28/2019	8/28/2019				
74	Submit SOQs	0 days	9/23/2019	9/23/2019	9/23/2019				
75	Review SOQs	16 days	9/23/2019	10/14/2019					
76	Recommend Prequalified Subcontractors to SBC	0 days	10/16/2019	10/16/2019	10/16/2019				
77	Issue Notification Letters to Prequalified Subcontractors	0 days	10/17/2019	10/17/2019	10/17/2019				
78	Construction Documents Complete Package No. 3	59 days	12/3/2019	2/26/2020					
79	Submit Advertisement to Central Register and Newspaper	0 days	12/3/2019	12/3/2019	12/3/2019				
80	Notice in Central Register	0 days	12/11/2019	12/11/2019	12/11/2019				
81	Trade Contractor Bid	24 days	12/18/2019	1/22/2020					
82	Pre-Bid Meeting	0 days	1/8/2020	1/8/2020	1/8/2020				
83	Trade Contractor Bid Due	0 days	1/22/2020	1/22/2020	1/22/2020				
84	CM Develop GMP	21 days	1/22/2020	2/19/2020					
85	GMP Approval	0 days	2/26/2020	2/26/2020	2/26/2020				

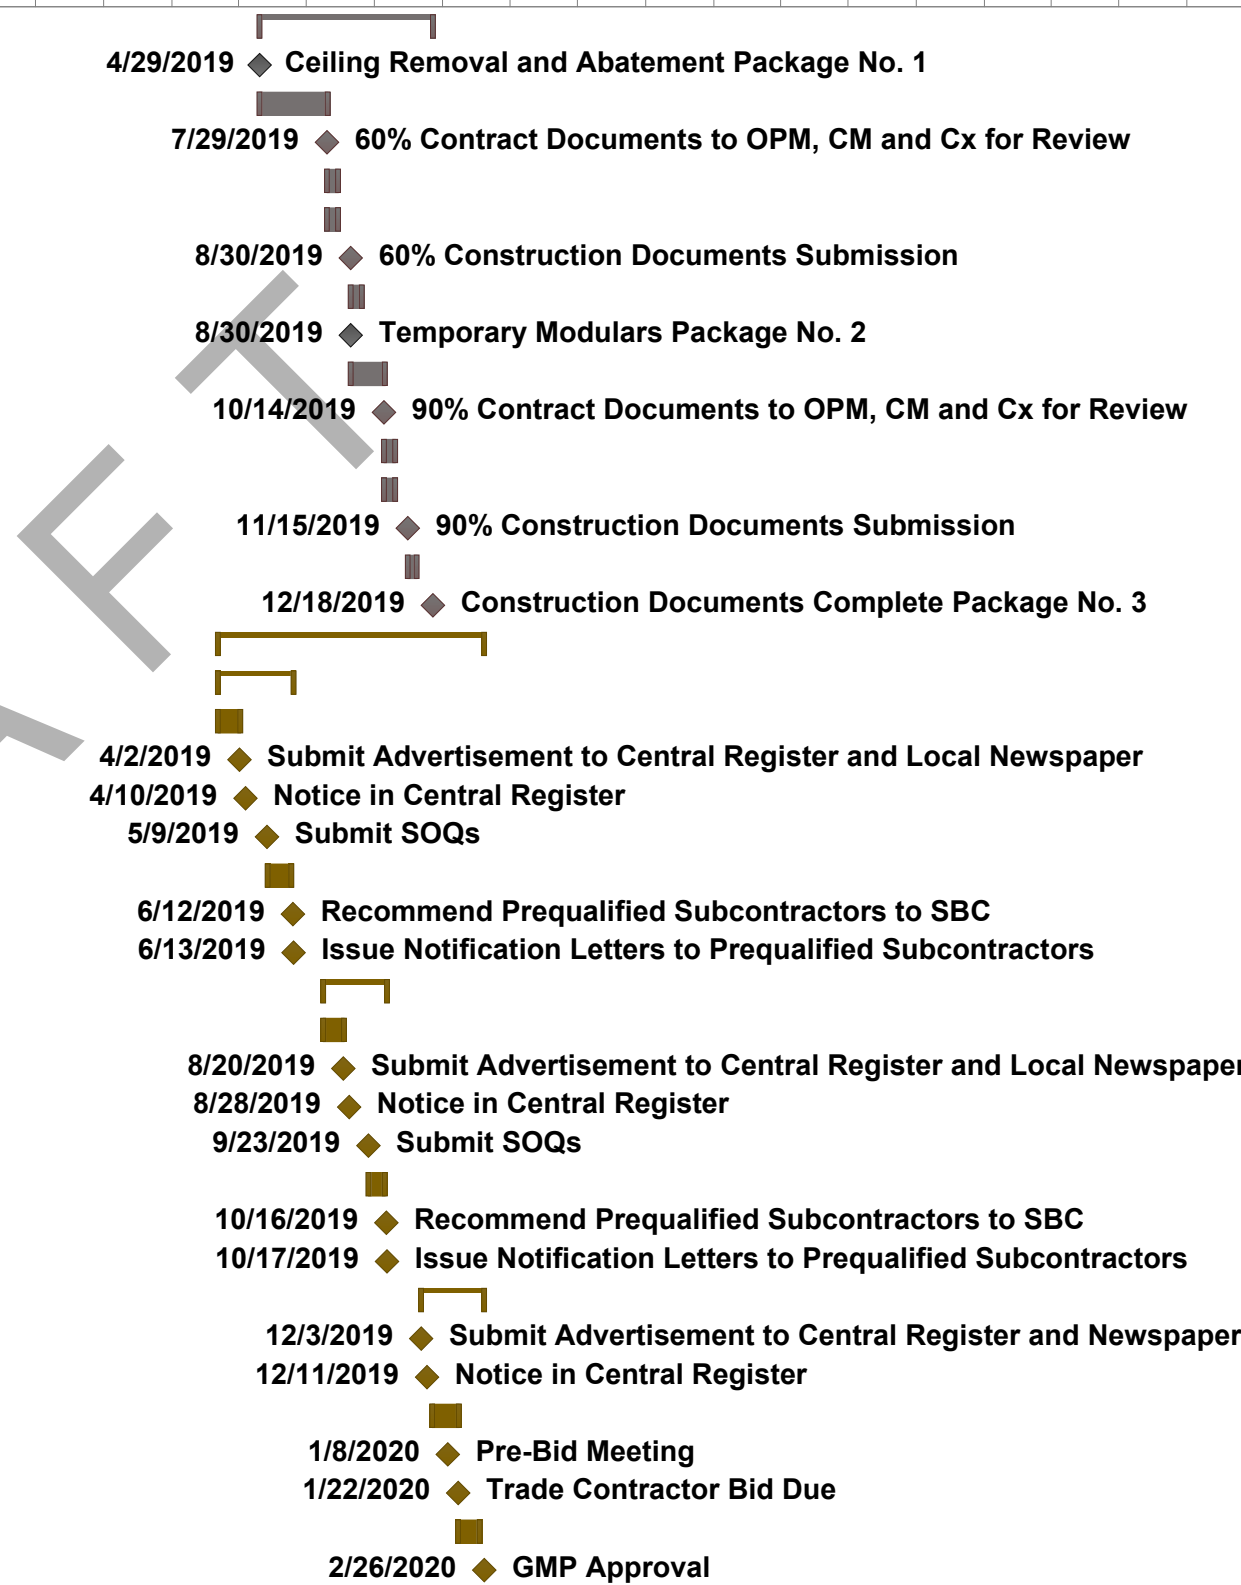

Revitalization of the Lincoln School
 Preliminary Project Schedule
 Design Development to Construction Phase



ID	Task Name	Duration	Start	Finish	2019	2020	2021	2022	2023
86	EARLY PACKAGES PROCUREMENT	115 days	4/29/2019	10/9/2019					
87	Ceiling Removal and Abatement Package No. 1	27 days	4/29/2019	6/5/2019					
88	CM Bid Ceiling Removal and Abatement Package No. 1	16 days	4/29/2019	5/20/2019					
89	Develop Ceiling Removal and Abatement Package No. 1 GMP	12 days	5/20/2019	6/4/2019					
90	Award Ceiling Removal and Abatement Package No. 1 GMP	0 days	6/5/2019	6/5/2019					
91	Temporary Modulares Package No. 2	27 days	8/30/2019	10/9/2019					
92	CM Bid Temporary Modulares Package No. 2	15 days	8/30/2019	9/20/2019					
93	Develop Temporary Modulares Package No. 2 GMP	8 days	9/20/2019	10/1/2019					
94	Award Temporary Modulares Package No. 2 GMP	0 days	10/9/2019	10/9/2019					
95	CONSTRUCTION	758 days	6/20/2019	6/1/2022					
96	Package 1 Commencement	0 days	6/20/2019	6/20/2019					
97	Substantial Completion - Package 1	0 days	8/21/2019	8/21/2019					
98	Package 2 Commencement	0 days	11/1/2019	11/1/2019					
99	Substantial Completion - Package 2	0 days	5/1/2020	5/1/2020					
100	Package 3 Commencement	0 days	6/20/2020	6/20/2020					
101	Substantial Completion - Phase 1 - Package 3	0 days	6/1/2021	6/1/2021					
102	Substantial Completion - Phase 2 - Package 3	0 days	6/1/2022	6/1/2022					

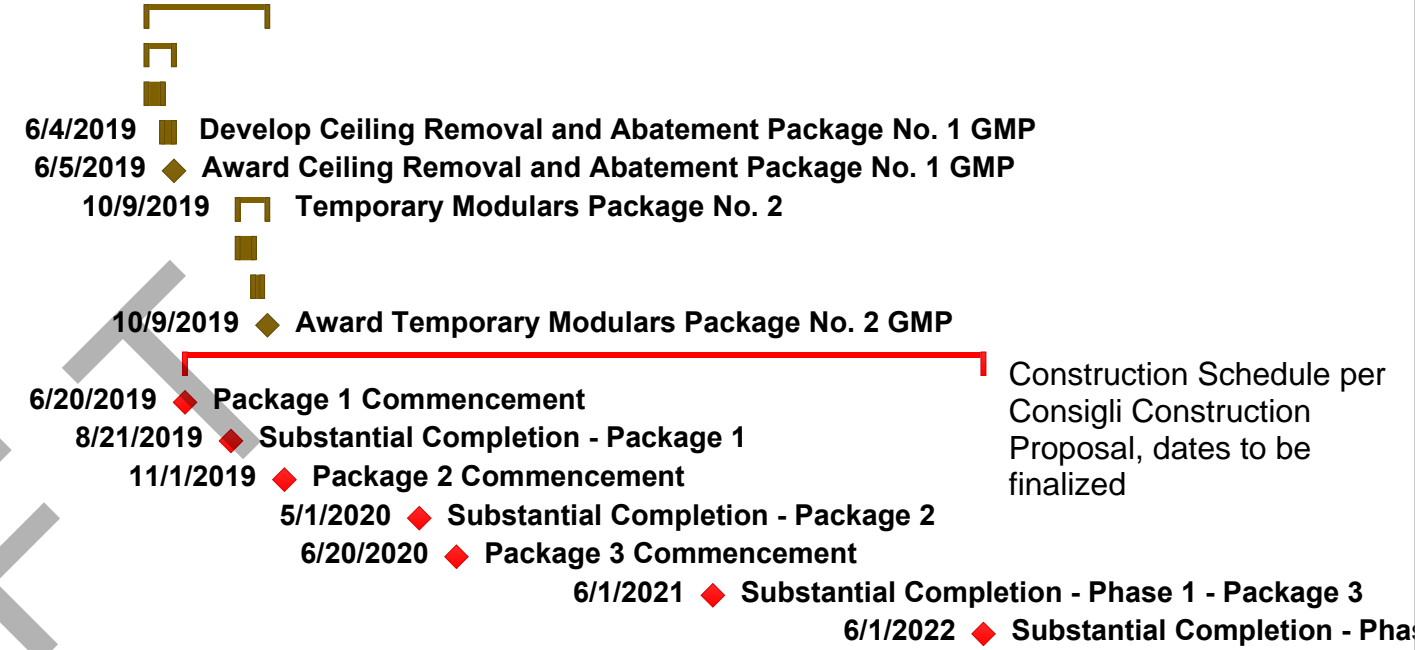

Construction Schedule per Consigli Construction Proposal, dates to be finalized

DRAFT
